# APPROVAL, CONTROL AND DISTRIBUTION PROCEDURE USING IUI PORTAL PROJECT 16057 PARS Iran

**INDEX**


1. PURPOSES AND SCOPE

2. DOCUMENTS ELECTRONIC APPROVAL

3. APPROVAL WORKFLOWS FOR THE PROJECT

4. INSTRUCTIONS

5. ELECTRONIC DISTRIBUTION OF DOCUMENTS

APPENDIX 1.Audit

APPENDIX 2. Approval WORKFLOWS structure.

APPENDIX 3.Document type's properties: IUI_Documento_de_Proyecto

APPENDIX 4.Approved documents daily transmission (TRANSMITTAL)


| | | | | |
|---|---|---|---|---|
| ALBR | CPA / AMM / JJDP | 01 | 19/02/2003 | FOR APPROVAL AND/OR COMMENTS |
| APROV. | VERIF. | EDITION | DATE | EDITED FOR |

## 1. PURPOSE AND SCOPE

This procedure's purpose is to describe documents **introduction, approval** and **distribution** using IUI's Portal for **16057 PARS Iran Project**

## 2. DOCUMENTS ELECTRONIC APPROVAL

IUI's Portal allows designing **Approval Flows (WORKFLOWS)** which send automatically the documents to the person who is responsible for their verification or approval.

By means of the electronic approval circuits, we relate documents to a LIFE CYCLE which consists of a succesion of approval states. As the approval workflow progresses the document state changes.

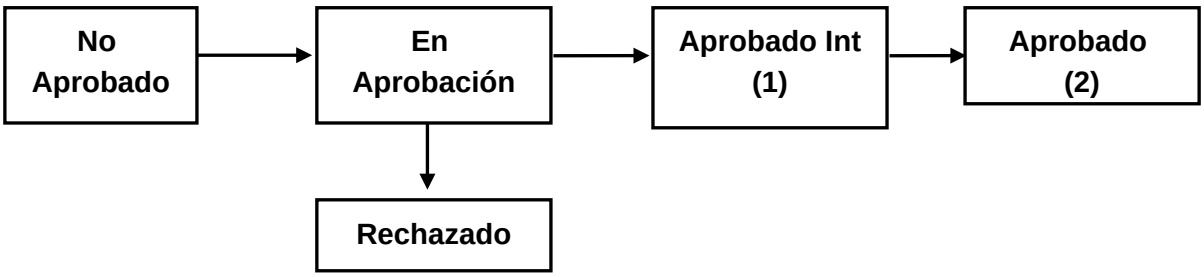


- **No aprobado.** Not yet approved
- **En aprobación.** In approval
- **Rechazado.** Rejected
- **Aprobado Int.** Internally approved (by EPC Contractor but not yet by the Client)
- **Aprobado.** Final approved

**Any approval or reject action requires performer's personal password and it's recorded in a register called Audit. (APPENDIX 1)**

Using electronic approval we intend to:

- **Control document's status and document's approval process:** At anytime you can look up every document's status, this means, whether it's finally approved, approved just by IUI…In addition, every approval or reject action is registered in the audit of the document.
- **Information safety:** once a document is **approved** it's protected from any deleting or overwriting action, but you can import a new document version keeping accessible the previous ones. With this protection, many users can work with the document and update it because the approved version is protected.
- **Real time information access:** Documents are included in the system before approving. So when the approval circuit is completed and its distribution is made, the documents are instantaneously available.

***VERY IMPORTANT: For electronic approval you use personal user password, so it is a KEY SAFETY REQUIREMENT that this password is only known by its owner. It's forbidden to share passwords.***

## 3. APPROVAL WORKFLOWS FOR THE PROJECT

There are two different **APPROVAL WORKFLOWS**

- A specific one for **Material Supplies Documents (requisiciones de material or RM in spanish)**
- The other for any other **document approval**

These WORKFLOWS **will always be initiated by the Discipline Leader (DL)** responsible for the document, the only person allowed.

Then the WORKFLOW starts, the following steps are defined in the **INSTRUCTIONS.**

The difference between both workflows is that the **Material Supplies (RM) one requires an additional step**.

A **Material Supply Document (RM)** is the **technical specification** of a certain **supply** of equipment or materials, specification that is sent to the suppliers as a request of quotation or as a contractual attachment to the purchase order.

A RM is a **compund document** that consists of the **RM document itself** and the **set of attached documents** listed in the RM document. **To make available this set of documents to the suppliers** via Internet the **Project Administrator must put them together in the same folder**.

Due to it, **before the approval steps, an additional step is required** in the workflow so that **Project Administrator receives the RM Document and puts together it and its attached documents** in the same folder.

The **access of the suppliers** to the documents is **controlled by the approval workflow**, so that **in the moment of the internal approval the Project Management Team can choose between publishing or not** in IUI Business Center (IUI eBusiness Portal). Anyway, suppliers can access the documents when they are finally approved by the client.

(APPENDIX 2. Approval cycles (WORKFLOWS) structure.)

## 4. INSTRUCTIONS

These are the following steps or actions in the 16057 PARS Iran Project WORKFLOW.

| ACTIONS | RESPONSIBLE |
|---|---|
| 1) **Previous checkings** to the document content:<br>- **Includes** the **revision number and date, reason for issue** and **the short name of the authors, reviewers and approvers.**<br>- The **printing area** is well configured.<br>- **The document contains not macros not even external links** (specially applicable to Excel workbooks). | **AUTHOR** |
| 2) **PARTICULAR CASE:** If the document is a **technical drawing (AutoCAD .dwg or microstation .dgn) a PDF rendition (Acrobat version) should be created so that it can be** | **AUTHOR** |

| ACTIONS | RESPONSIBLE |
|---|---|
| **imported later** close to the document native format. | |
| **3) DOCUMENT INCORPORATION TO IUI PORTAL:**<br><br>**(** Handbook **MN-GC-I-02. ACCIONES BÁSICAS** issued by IUI's Knowledge Management Department**)**<br><br>- **CASE 1: The document is issued for the first time**<br>• **Selects the right folder** where the document should be located.<br>• **Imports the document** into the folder.<br>• **Fills in document's properties**. (**Appendix 3**)<br>• **Imports (dwg** ó **dgn) or creates (other formats) the PDF rendition**<br><br>- **CASE 2:** The document is a **new issue of an existing document (there are previous revisions of the document in IUI Portal).**<br>• **Locates the document** in IUI Portal<br>• **Incorporates** the new issue of the document **as a new version of the existing ones** (check-out / check-in)<br>• **Fills in document's properties**. (**Appendix 3**)<br>• **Imports (dwg** ó **dgn) or creates (other formats) the PDF rendition** | **AUTHOR** |
| **4) Warning** to the Discipline Leader so that he/she finds out that the **document is ready to send it for approval.** *(the way recommended is using IUI Portal's documents routing tool is)* | **AUTHOR** |
| **5) Verification:** Checks if the document is ready to send it for approval | **DISCIPLINE LEADER** |
| **6) Initiates approval workflow.** Before that, chooses the right workflow depending on if the document is a RM or not. | **DISCIPLINE LEADER** |

| ACTIONS | RESPONSIBLE |
|---|---|
| ***7) For the RM specific WORKFLOW:***<br>• Create the RM folder<br>• **Link** the attached documents to the folder<br>**(** MN-GC-I-08. GUÍA DE COMERCIO ELECTRÓNICO PARA ADMINISTRADORES DE PROYECTO( Project Administrator e-business handbook)**)** | **PROJECT ADMINISTRATOR** |
| **8)** Any member of the **Project Management Team** (the Project Engineers or the Project Manager) can approve or reject the document. They have the following options:<br>• **Internal approval *(Aprobado int** in spanish)* waiting for the client to approve or reject<br>• **Internal approval and publishing,** waiting for the client to approve or reject, but in this case the document becomes available to the suppliers.<br>• **Approve *(Aprobado** in spanish)*. Selected option for those documents which approval by the client is not required (IUI can perform the final approval).<br>• **Reject *(Rechazado** in spanish)*. The workflow finishes so that the author can edit the document to correct it.<br><br>There is a **Common Inbox** for all members of the Project Management Team where they receive the documents for approval. When one of them opens a certain approval task from the common inbox, it moves to his personal inbox. When someone opens an approval task and it's another one's duty, he/she can **reassign** it to the right person. | **PROJECT MANAGEMENT TEAM** |
| **9) Client's approval.** After the document is checked, the client assigns an approval status to it. This status is registered by the Project Administrator. The options are:<br>• **Approved without comments *(Aprobado SC** in spanish).*<br>• **Approved with comments *(Aprobado CC).*** | **PROJECT ADMINISTRATOR** |

| ACTIONS | RESPONSIBLE |
|---|---|
| • **Rejected (*Rechazado*)** | |

**When a document is in a workflow, it is not possible to incorporate a new version** of the document**.**

Due to it, **ONLY IN THE EXCEPTIONAL CASE in which the client has not approved yet the document and the Discipline Leader needs to incorporate a new version of that document**, **the Discipline Leader can finishes the workflow** by executing a finish task for that workflow available in his/ her personal Inbox.

## 5. ELECTRONIC DISTRIBUTION OF DOCUMENTS

By means of the **approval status** and the **approval dates** of the documents registered in the system, **we can determine daily which documents must be distributed** to the different members of the project since last distribution.

So, **Project Administrator will perform a daily distribution** in the following manner:

- **Obtains from IUI Portal a list that contains the documents that must be distributed (**those approved since last distribution date). In that list, documents will be ordered by Activity (actividad) and then by type (clase) (Appendix 3) .
- **Sends an email with the documents list attached** (this would be the transmittal) to the members of the project so that they find out about the availability of the listed documents in IUI Portal.

In Appendix 4 there is an example of the transmittal format.

**APPENDIX 1.** **Audit**

**Estado: Aprobado** *status: Approved*

**Aprobado SC** *approved without comments*

**Editado para:** Petición de Oferta *edited for: Request for Inquiry*

**Documento:** **REQ-102-F00-0**
*(Document)*
**Título:** Storage Spheres
*(Title)*
**Edición:** 01
*(Version)*
**Departamento:** Mecánica
*(Department: Mechanical)*
**Descripción:** Requisición de Esferas
*(Description)*

**OT:** 16057 PARS Iran
*(Project)*
**Fecha de aprobación:** 08/02/2003
*(approval date)*
**Fecha de revisión Cliente:** 14/02/2003
*(clients approval date)*

*Histórico de estados del documento*

*Documents status register*

| **Tipo** *(type)* | **Fecha** *(Date)* | **Responsable** *(Responsible)* | **Acción** *(Action)* | **Cargo** *(Position)* |
|---|---|---|---|---|
| PROYECTO | 07/02/2003 | Cámara Cámara, Sonia | Envío a aprobación *(Send for approval)* | Responsable de cuenta *(Project Department Leader)* |
| | 08/02/2003 | Brignardello, Aldo | Aprobación *(Approval)* | Jefe de Proyecto IUI *(IUI Project Manager)* |
| | 14/02/2003 | López Rubio, Verónica | Aprobado SC *(PARS approval without comments register)* | Administrador de Proyecto *(Project Admin)* |

## APPENDIX 2. Approval WORKFLOWS structure.

### Workflow 1. General approval.

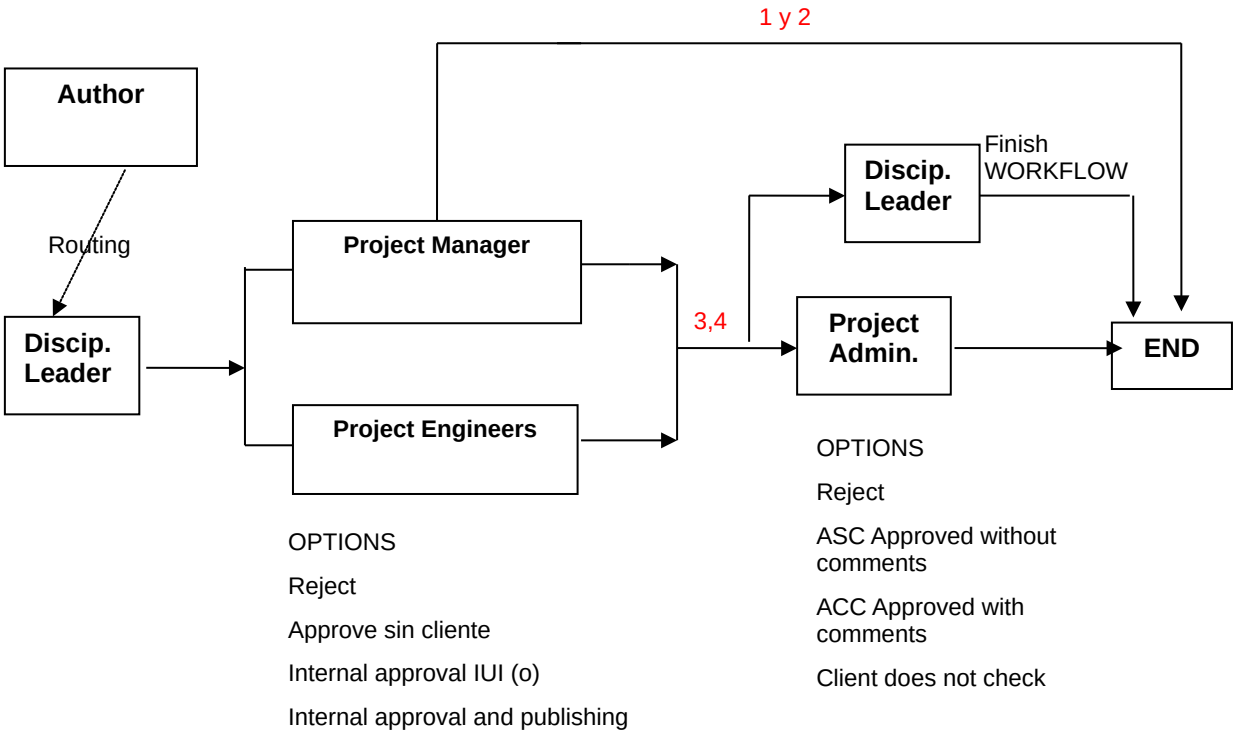


### Workflow 2. RM (Material Supply Document) approval.

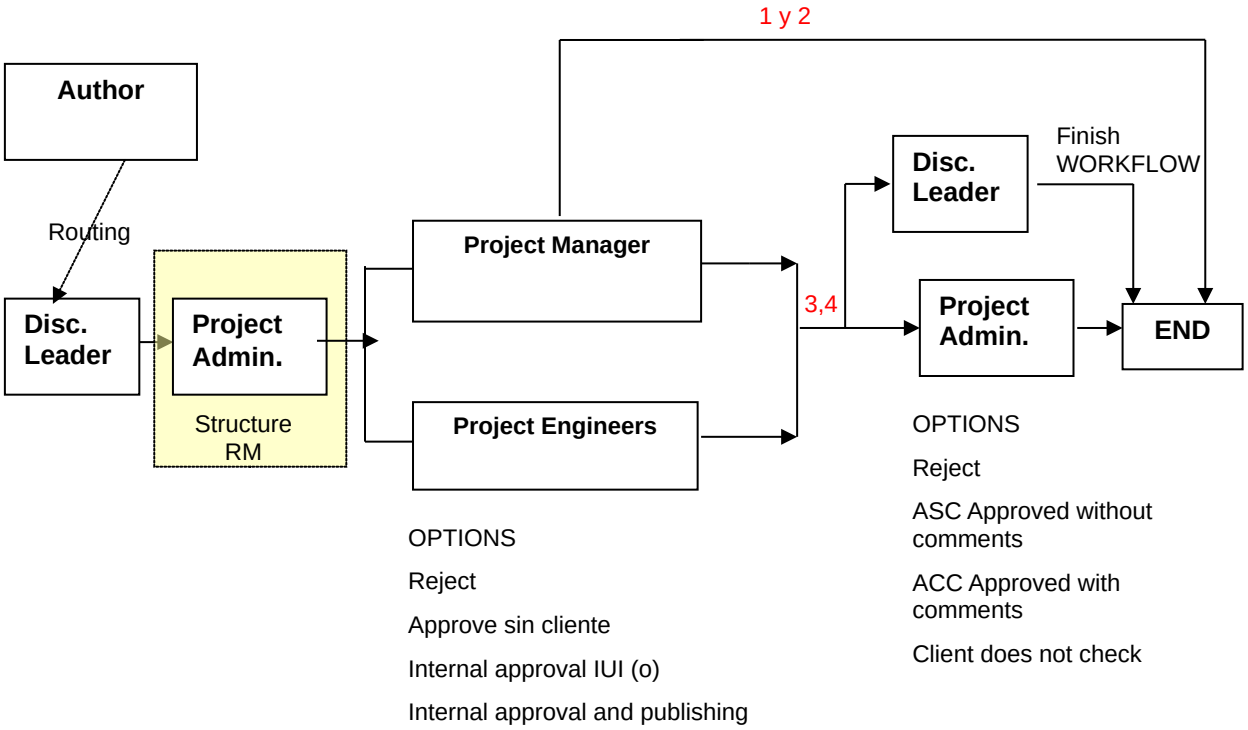

**APPENDIX 3. Document type's properties:** IUI_Documento_de_Proyecto

The following are **properties or attributes** which are linked to every document filled in when you import a document. Also if there is a new version you would only have to change the shaded properties because the others won't change and are inherited from the first version.

| Properties | Description | Example |
|---|---|---|
| ***DOCUMENTO***<br>*Max 255 characters* | Document's identification. | **REQ-102-EQ-F00-0** |
| ***TITULO***<br>*Max 255 characters* | Title | **STORAGE SPHERES** |
| ***EDICION***<br>*Max 3 characters* | Revision number | **00** |
| ***FECHA***<br>*Max 32 characters* | Documents revision date (format dd/mm/yyyy) | 07/02/2003 |
| ***EDITADO PARA***<br>List | what is the document issued for | **Petición de Oferta** |
| ***AUTORES***<br>*Max 32 characters for each author* | Document author. Name and Surname | **Sonia Cámara Cámara** |
| ***OT***<br>*List* | Project identification | **16057-PARS Irán** |
| ***DEPARTAMENTO***<br>*List* | Department | **Mecánica** |
| ***CLASE***<br>*List* | Documents special type (data sheet, drawing, list…) | **RM / RC** |
| ***ACTIVIDAD***<br>*List* | Department's different activities (rotating equipment, piping, electrical…) | **32 - EQUIPOS ESTATICOS** |
| ***IDIOMA***<br>*List* | Document's language (default: Spanish) | **Inglés** |
| ***DESCRIPCION***<br>*Max 255 characters* | If it's needed additional description | **Requisición de Esferas** |
| ***PALABRAS CLAVE***<br>*Max 32 characters for every concept* | Keywords | **esferas** |

## APPENDIX 4. Approved documents daily transmission (TRANSMITTAL)

| INTECSA UHDE | DOCUMENTOS INCORPORADOS AL PORTAL | | | | PROYECT0 | 16057 - PARS Irán |
|---|---|---|---|---|---|---|
| | | | | | CLIENTE | PARS Petrochemical co. |
| | | | | | TRANSMITTAL | 2 |
| | | | | | FECHA | 10/02/2003 |
| | | | | | EDITADO POR | Juan José Díez Peña |
| Actividad | Clase | ID documento | Descripción | Rev | Editado para | Fecha de Edición |
| 00 - GENERAL | Especificación | 16057-IT-01 | PROCEDIMIENTO DE USO DEL PORTAL EN EL PROYECTO 16057 - PARS Irán | 1 | Aprobación y/o comentarios | 03/12/2002 |
| 00 - GENERAL | Especificación | 16057-IT-01 (I) | PORTAL USE PROCEDURE - 16057 PARS Irán PROJECT | 1 | Aprobación y/o comentarios | 03/12/2002 |
| 00 - GENERAL | General | NUMBERING & CODING SYSTEM | | 0 | Aprobación y/o comentarios | 18/12/2002 |
| 32 - EQUIPOS ESTATICOS | Planos de Equipo | DWG-EQ-30-1001 | PROPYLENE SPHERE- 60-D-3040 | A | Aprobación y/o comentarios | 05/02/2003 |
| 32 - EQUIPOS ESTATICOS | Planos de Equipo | DWG-EQ-30-1002 | PROPYLENE SPHERE DETAILS - 60-D-3040 | A | Aprobación y/o comentarios | 05/02/2003 |
| 32 - EQUIPOS ESTATICOS | Planos de Equipo | DWG-EQ-30-1005 | PROPANE SPHERE - 60-D-3030 | A | Aprobación y/o comentarios | 05/02/2003 |
| 32 - EQUIPOS ESTATICOS | Planos de Equipo | DWG-EQ-30-1006 | PROPANE SPHERE DETAILS - 60-D-3030 | A | Aprobación y/o comentarios | 05/02/2003 |
| 40 - ELECTRICIDAD | Especificación | E-N-08 | MOTORES ELÉCTRICOS DE INDUCCIÓN | 2 | | 01/07/2000 |
| 50 - INSTRUMENTACION | Especificación | EC-K-21 | ESPECIFICACIÓN GENERAL DE MONTAJE DE INSTRUMENTOS | 3 | | 01/11/1998 |
